



Weekly Project Update – August 1, 2019

# 4th street revitalization

Stay Updated. Find us online.



A Virtual Flythrough of the project is available for viewing and downloading to your website at [www.losranchosnm.gov](http://www.losranchosnm.gov)

For questions or concerns, please contact the Village of Los Ranchos at 505-344-6582 or at 6718 Rio Grande Blvd., NW

## Construction Activity

### Sidewalks and On-Street Parking in the Promenade

Bricklaying crews with the subcontractor Beaty Masonry are now working on the sidewalks in the promenade. Beaty Masonry also continues the installation of the permeable paver system in the gutter pan south of Pueblo Solano Rd. The brick sidewalks and the permeable paver system are anticipated to be complete by the end of August.


The subcontractor MWI continues the installation of pedestrian light poles beyond Green Valley Rd. All light poles are scheduled to be installed by mid-August. Stormwater piping installation to the drainage reservoir on Schulte Rd. will begin this week.

Construction on the west side of Fourth Street began on April 8<sup>th</sup> and is on schedule for projected completion in September of this year.

Maria G. Rinaldi, Project Manager  
505-344-6582/505-379-8982 cell  
[mrinaldi@losranchosnm.gov](mailto:mrinaldi@losranchosnm.gov) [info@losranchosnm.gov](mailto:info@losranchosnm.gov)



Beaty Masonry bricklaying crew installing brick sidewalk in the Promenade.

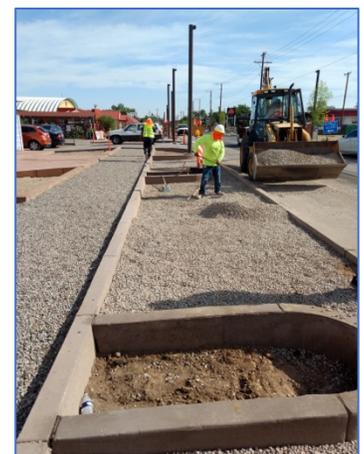

Bradbury Stamm crew prepping basecourse for on-street parking.

2018  
4TH STREET PROJECT

VILLAGE OF LOS RANCHOS DE ALBUQUERQUE

The 4<sup>th</sup> Street Project Office at 338 Osuna is open to the public Tuesdays-Thursday 9:00am-4:00pm or by appointment. The office is intermittently closed for meetings.
