


ID	Task Name	Duration	Start	Finish	Aug 24, '14				Aug 31, '14				Sep 7, '14				Sep 14, '14				Sep 21, '14											
					W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S			
1	PRE-CONSTRUCTION	7 days	Wed 8/20/14	Fri 8/29/14	PRE-CONSTRUCTION																											
2	NOTICE TO PROCEED	0 days	Wed 8/20/14	Wed 8/20/14	NOTICE TO PROCEED																											
3	NOTIFY	2 days	Fri 8/22/14	Fri 8/29/14	NOTIFY																											
4	POST SIGNS	1 day	Wed 8/27/14	Wed 8/27/14																												
5	CONSTRUCTION	60 days	Tue 9/2/14	Mon 11/24/14																												
6	MOBILIZATION	2 days	Tue 9/2/14	Wed 9/3/14	MOBILIZATION																											
7	SWPPP INSTALL	1 day	Thu 9/4/14	Thu 9/4/14	SWPPP INSTALL																											
8	SURVEY STAKING	1 day	Fri 9/5/14	Fri 9/5/14	SURVEY STAKING																											
9	DEMOLITION	10 days	Mon 9/8/14	Fri 9/19/14	DEMOLITION																											
10	SAW CUT ASPHALT & CONCRETE	1 day	Mon 9/8/14	Mon 9/8/14	SAW CUT ASPHALT & CONCRETE																											
11	REMOVE CURB GUTTER	1 day	Tue 9/9/14	Tue 9/9/14	REMOVE CURB GUTTER																											
12	REMOVE CONCRETE SIDEWALK	1 day	Wed 9/10/14	Wed 9/10/14	REMOVE CONCRETE SIDEWALK																											
13	REMOVE ASPHALT STREET	1 day	Thu 9/11/14	Thu 9/11/14	REMOVE ASPHALT STREET																											
14	EXCAVATION	6 days	Fri 9/12/14	Fri 9/19/14	EXCAVATION																											
15	SUB-GRADE	20 days	Mon 9/22/14	Fri 10/17/14																												
16	GRADE FOR CONCRETE SUB-GRADE	9 days	Mon 9/22/14	Thu 10/2/14	GRADE FOR CONCRETE SUB-GRADE																											
17	AB FOR WALLS AND CURB	2 days	Thu 10/9/14	Fri 10/10/14	AB FOR WALLS AND CURB																											
18	AB FOR SIDEWALK	1 day	Mon 10/13/14	Mon 10/13/14	AB FOR SIDEWALK																											
19	BACKFILL CUTOFF WALLS AND GRADE FOR SHOULDER	1 day	Fri 10/17/14	Fri 10/17/14	BACKFILL CUTOFF WALLS AND GRADE FOR SHOULDER																											
20	PAVING PCC & AC	15 days	Fri 10/3/14	Thu 10/23/14																												
21	CUTOFF WALL - FORM POUR & CURE	4 days	Fri 10/3/14	Wed 10/8/14	CUTOFF WALL - FORM POUR & CURE																											
22	CURB GUTTER - FORM POUR & CURE	4 days	Mon 10/13/14	Thu 10/16/14	CURB GUTTER - FORM POUR & CURE																											
23	SIDEWALK - FORM POUR & CURE	3 days	Mon 10/20/14	Wed 10/22/14	SIDEWALK - FORM POUR & CURE																											
24	ASPHALT CONCRETE	1 day	Thu 10/23/14	Thu 10/23/14	ASPHALT CONCRETE																											
25	DRAINAGE	16 days	Fri 10/24/14	Fri 11/14/14																												
26	BIO-SWALE DRAIN ROCK	3 days	Fri 10/24/14	Tue 10/28/14	BIO-SWALE DRAIN ROCK																											
27	4" PERFORATED & SOLID PVC PIPE	3 days	Mon 10/27/14	Wed 10/29/14	4" PERFORATED & SOLID PVC PIPE																											
28	ASPHALT PATCH TRENCH	1 day	Thu 10/30/14	Thu 10/30/14	ASPHALT PATCH TRENCH																											
29	BIO-SWALE SOIL	3 days	Thu 10/30/14	Mon 11/3/14	BIO-SWALE SOIL																											
30	STREAMBED COBBLES	2 days	Tue 11/4/14	Wed 11/5/14	STREAMBED COBBLES																											
31	LANDSCAPING	7 days	Thu 11/6/14	Fri 11/14/14	LANDSCAPING																											
32	SITE FURNISHINGS & STRIPING	6 days	Mon 11/17/14	Mon 11/24/14																												
33	EDUCATIONAL SIGNS	1 day	Mon 11/17/14	Mon 11/17/14	EDUCATIONAL SIGNS																											
34	PEDESTRIAN BOARDWALKS	5 days	Mon 11/17/14	Fri 11/21/14	PEDESTRIAN BOARDWALKS																											
35	STRIPING & MARKINGS	1 day	Mon 11/24/14	Mon 11/24/14	STRIPING & MARKINGS																											

GREEN STREET IMPROVEMENT PROJECT CARLOS STREET, MOSS BEACH, CA Date: Mon 8/25/14	Ryan Barrett ryan@igpinc.com Interstate Grading and Paving, Inc.	Task		External Tasks		Manual Task		Finish-only		Deadline
		Split		External Milestone		Duration-only		Manual Summary Rollup		Progress
		Milestone		Inactive Task		Manual Summary		Inactive Milestone		Manual Summary
		Summary		Inactive Milestone		Manual Summary		Inactive Summary		Start-only
		Project Summary		Inactive Summary		Start-only				

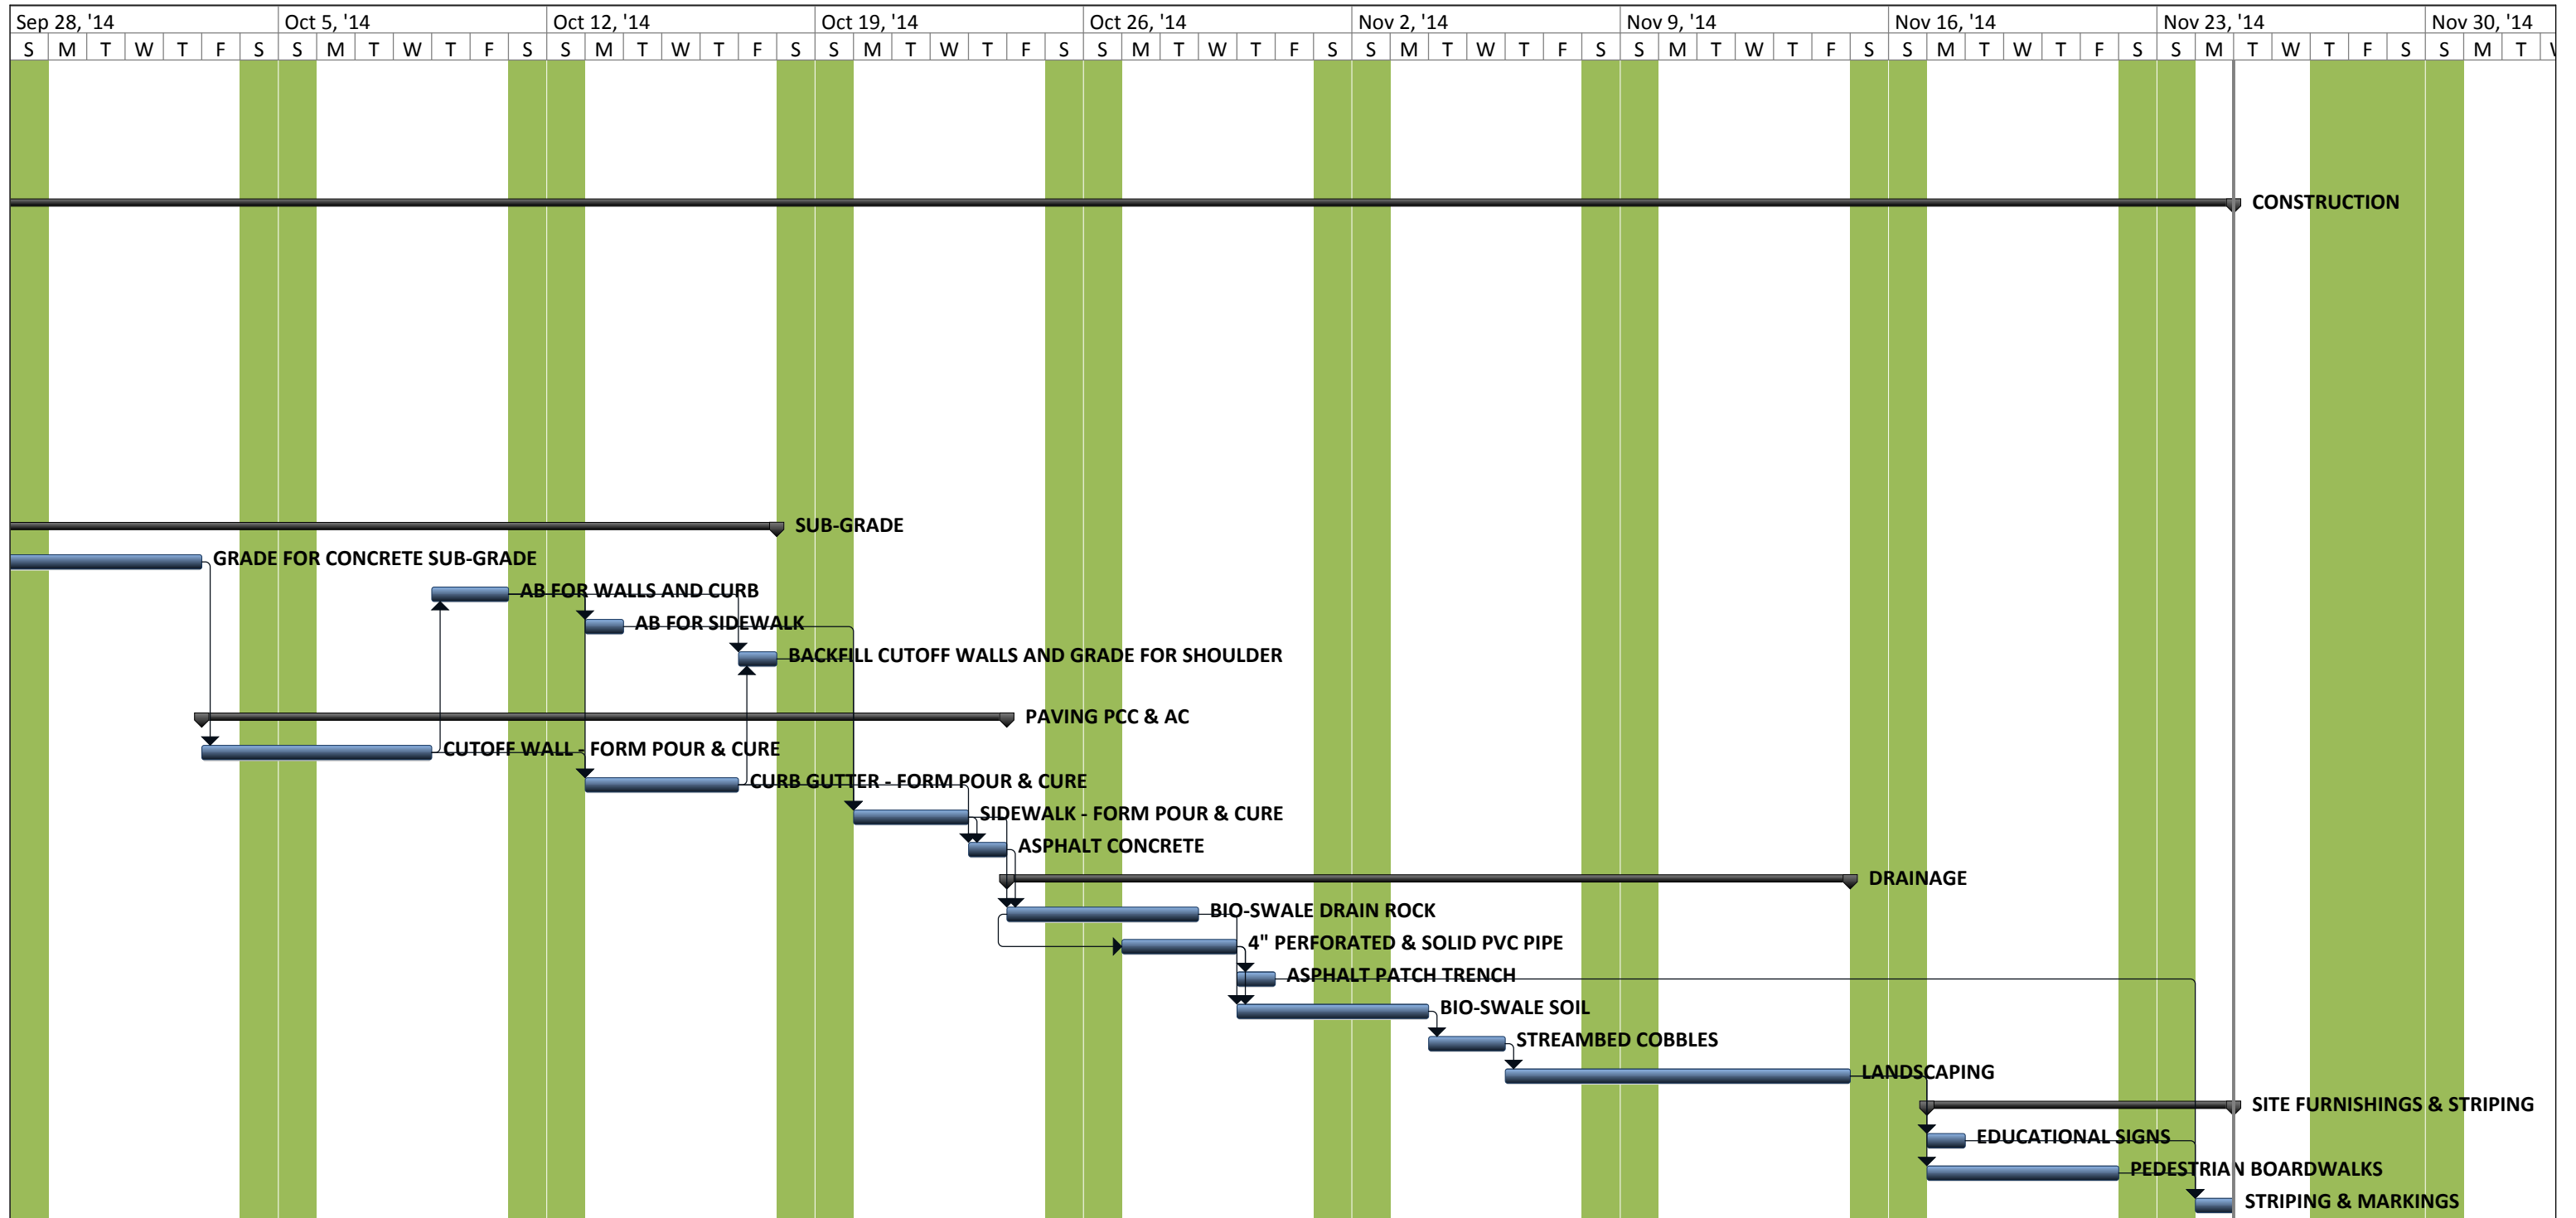

GREEN STREET IMPROVEMENT PROJECT
 CARLOS STREET, MOSS BEACH, CA
 Date: Mon 8/25/14

Ryan Barrett
 ryan@igpinc.com
 Interstate Grading and Paving, Inc.

Task		External Tasks		Manual Task		Finish-only		Deadline
Split		External Milestone		Duration-only		Deadline		Deadline
Milestone		Inactive Task		Manual Summary Rollup		Progress		Deadline
Summary		Inactive Milestone		Manual Summary		Progress		Deadline
Project Summary		Inactive Summary		Start-only		Progress		Deadline
