

CONSTRUCTION TESTING & ENGINEERING, INC.

P.O. BOX 271125, SALT LAKE CITY, UTAH 84127-1125
(801) 972-4001 • Construction.Testing@gmail.com

SOILS TEST REPORT


CLIENT: Lakeview Rock Products
PROJECT: QC Testing, Upper Pit
RE: 2" Gravel
SPECIFICATION REQUIREMENTS: See target below

DATE: January 26, 2022, Wed.
FILE #: 125 / WO #: 7190

SIEVE ANALYSIS RESULTS ASTM C 136

Sieve Size	Sieve Opening in mm	Individual % Retained	Accumulated % Retained	**RESULTS** % Passing	Ideal /Tolerance Gradation % Passing
2"	50.0	0	0	100	100
1"	25.0	82.0	82.0	18.0	NA
3/4"	19.0	13.2	95.2	4.8	"
1/2"	12.5	1.3	96.5	3.5	"
3/8"	9.5	.1	96.6	3.4	"
#4	4.75	.1	96.7	3.3	"

Test sample dry weight: 5619 grams (split sample)

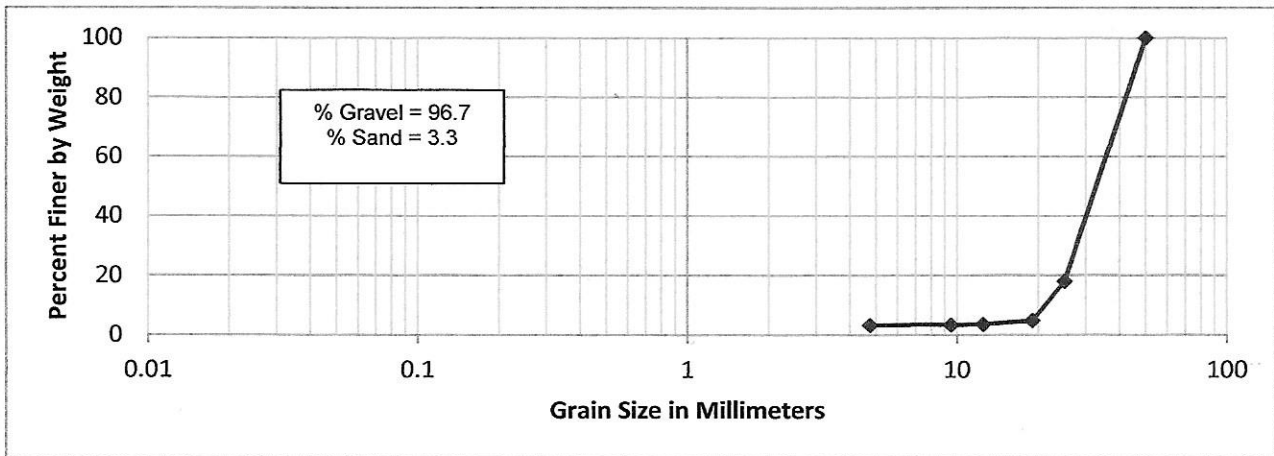

REMARKS:

Source of material: Upper Pit stockpile
Moisture content as received: 2.4%
Gravel physical appearance/shape: Angular

CONSTRUCTION TESTING & ENGINEERING, INC.
CERTIFIED TEST REPORT:

David K. Megeath, Manager
