Devils Slide Construction Timeline Rev 7-13-12

ID	Task Name	Duration	Start	Finish
1	**Estimated Tunnel Opening**	0 days	Sat 1/5/13	Sat 1/5/13
2	**Estimated Lot Completion**	0 days	Sat 4/6/13	Sat 4/6/13
3	**Trail and Lot Opening**	0 days	Sat 1/4/14	Sat 1/4/14
4				
5				
6	**Capital Construction**			
7	Prepare Design RFP	15 days?	Mon 7/2/12	Fri 7/20/12
8	Advertise RFP	23 days?	Tue 7/24/12	Thu 8/23/12
9	Select Consultant	9 days?	Mon 8/27/12	Thu 9/6/12
10	Execute contract	10 days?	Mon 9/10/12	Fri 9/21/12
11	Prepare Concept Plans	19 days?	Tue 9/25/12	Fri 10/19/12
12	Concept Plan Review	10 days?	Mon 10/22/12	Fri 11/2/12
13	Public Meeting Prep	5 days?	Mon 11/5/12	Fri 11/9/12
14	Public Meeting	0 days	Tue 11/13/12	Tue 11/13/12
15	60% Plan Preparation	23 days?	Thu 11/15/12	Fri 12/14/12
16	Parks Commission	0 days	Thu 12/6/12	Thu 12/6/12
17	60% Plan Review	10 days?	Mon 12/17/12	Fri 12/28/12
18	Env Review/Permits	85 days?	Thu 1/3/13	Fri 4/26/13
19	90% Plans/Specs/timates	15 days?	Tue 1/1/13	Fri 1/18/13
20	90% Plan/Spec/Est Review	10 days?	Mon 1/21/13	Fri 2/1/13
21	Planning Commission	0 days	Wed 1/23/13	Wed 1/23/13
22	100% Plans/Specs/Estimate	15 days?	Mon 4/29/13	Fri 5/17/13
23	100% Plan/Spec/Est Review	10 days?	Mon 5/20/13	Fri 5/31/13
24	Prepare BOS Documents	10 days?	Mon 6/3/13	Fri 6/14/13
25	BOS Adopt and Bidding	0 days	Tue 6/25/13	Tue 6/25/13
26	Open Bids	0 days	Tue 7/16/13	Tue 7/16/13
27	Prepare BOS Award Docs	8 days?	Wed 7/17/13	Fri 7/26/13
28	BOS Award Contract	0 days	Tue 8/13/13	Tue 8/13/13
29	Execute contract	0 days	Mon 8/26/13	Mon 8/26/13
30	Construction	75 days?	Mon 8/26/13	Fri 12/6/13
31	Post Construction/Notices	17 days?	Mon 12/9/13	Tue 12/31/13
32				
33	**Other Capital/Equipment**			
34	Parking Lot Config w/CalTrans	45 days?	Mon 7/2/12	Fri 8/31/12
35	Execute Interpretative Sign Agreement	9 days	Tue 7/3/12	Fri 7/13/12
36	Prepare RFP for Interpretative Signs	10 days?	Mon 7/23/12	Fri 8/3/12
37	Advertise Sign RFP	25 days?	Mon 8/6/12	Fri 9/7/12
38	Spec/Purchase 2 Restrooms	10 days?	Mon 9/3/12	Fri 9/14/12
39	Select Interpretative Sign Contractor	10 days?	Mon 9/10/12	Fri 9/21/12
40	Develop Interpretive Signage	59 days?	Mon 9/24/12	Wed 12/12/12
41	Manufacture Intrepretative Signage	61 days?	Mon 11/26/12	Fri 2/15/13
42	Purchase Parking Lot Associated Equip	61 days?	Mon 1/7/13	Fri 3/29/13
43	Deliver Restrooms	20 days?	Mon 2/4/13	Fri 3/1/13
44	Intrepretative Sign Installation	20 days?	Mon 2/18/13	Fri 3/15/13
45	Noxious Weed Removal	131 days?	Mon 5/6/13	Fri 11/1/13
46	Purchase Trail Associated Equipment	132 days?	Mon 7/1/13	Tue 12/31/13
47				
48	**Operations Items**			
49	Purchase Lot Associated Supplies	65 days?	Wed 1/2/13	Fri 3/29/13
50	Hire Park Ranger II w/Lots	208 days?	Tue 3/19/13	Tue 12/31/13
51	Purchase Trail Associated Supplies	75 days?	Wed 9/18/13	Tue 12/31/13
52	Hire Park Ranger III and II w/Trail	12 days?	Mon 12/16/13	Tue 12/31/13

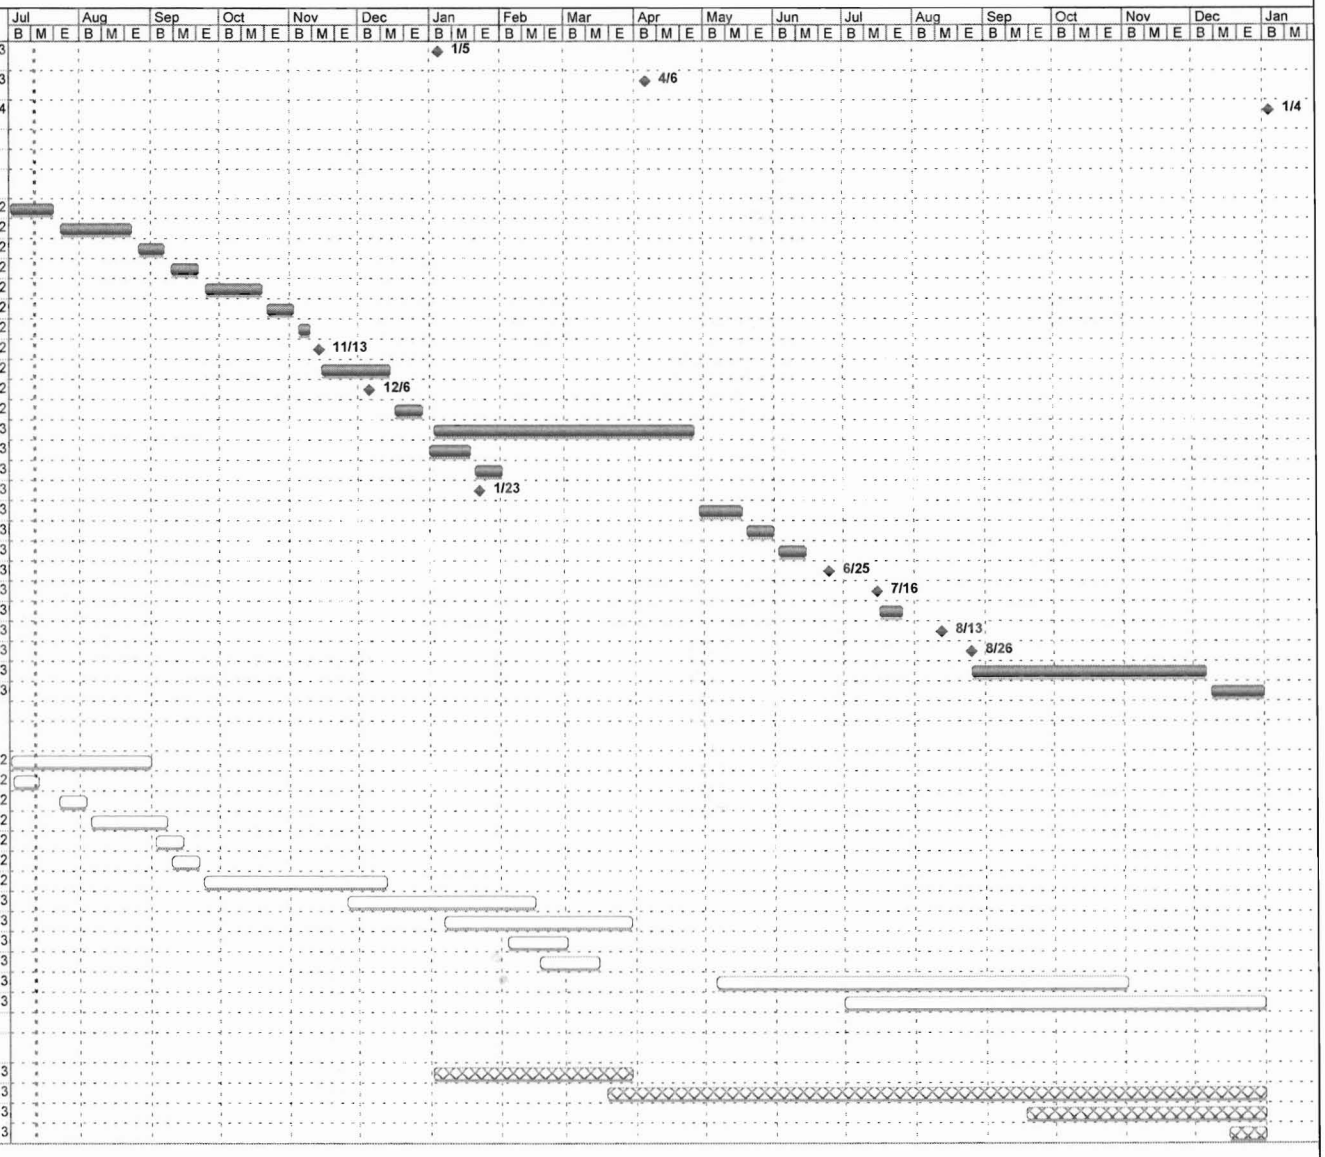

Project: Devils Slide Construction Tim
Date: Thu 7/12/12

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
